

# Seely's Cove Dredging

Seely's Cove, New Brunswick



## COMPLETION DATE

April 2010

## VALUE OF CONTRACT


\$1,484,485.00

## OWNER

Public Works & Government Services  
Canada

## CONSULTANT

Public Works & Government  
Services Canada

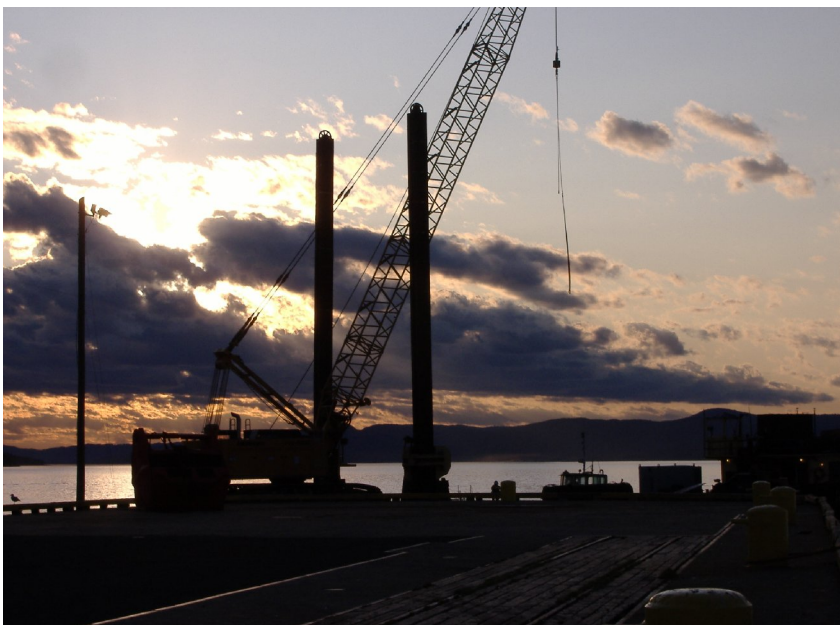

## Project Description

### DESCRIPTION

Dredging of 59,280 cmpm of Class B material in Seely's Cove, NB consisting of 52,270 cmpm of ocean dump disposal and 7,010 cmpm of land based disposal. Construction of a rock berm to contain Land Based dredge spoils.

### EQUIPMENT

"Willaim B. Dilly" Spud Barge  
Liebherr HS 885 Crawler Crane  
"Jamie L." Workboat  
"Delta II" Workboat  
"S.11" Dump Scow  
"FDJV3" Dump Scow

### INSTALLATION METHOD

Dredge spoils loaded into the dump scows with the Liebherr HS885 crane and transported to the unloading facility or ocean dump disposal site with the workboats.
